

[Subscribe](#)[Share](#) ▼[Past Issues](#)[Translate](#) ▼[News on the Germany Beck Project](#)[View this email in your browser](#)

Germany Beck Project

Weeks 31 & 32 commencing 9th January 2017

Happy New Year! This is the sixteenth edition of the newsletter that keeps you up to date with the progress of the Germany Beck junction works on the A19 in Fulford.

The last 2 weeks have seen little change as we prepared for the the Christmas closure

We have been carrying out some trial holes in the grassed area to the west of the A19 to confirm the position some services to the rear of the footpath and have commenced preparing for concrete works which form part of the retaining wall structure. Some temporary repairs have been carried out to the Fordlands Road footpath.


A temporary lighting tower has been erected on Fordlands Road by the Council's street lighting contractor whilst they investigate the faulty street light.

[Subscribe](#)[Share ▼](#)[Past Issues](#)[Translate ▼](#)

The anticipated site clearance works and piling in the vicinity of the Germany Beck culvert are now scheduled for the mid/end of January. The daily footpath closure as described below is expected to come into force week commencing 16th January.

In order gain access to the tree stumps we need to remove to complete the piling works adjacent to the Germany Beck A19 culvert we will be closing the footpath that runs along the east of the A19 between the hours of 9am and 3pm for a period of approximately 5 days. Having monitored the number of pedestrians using the footpath between those hours we know that this should not inconvenience many. However signs will be erected on Selby Road and Main Street to advise you of the footpath closure and a temporary pedestrian island will be installed at a point on Selby Road, as agreed by CYC, to aid those wishing to cross the A19 during those times.

You will also see traffic cones placed on the A19 which will reduce the width of the A19 slightly adjacent to the site. This is to provide our operatives with a safety zone between themselves and the traffic during the stump clearance works. Two way traffic will be maintained at all times.

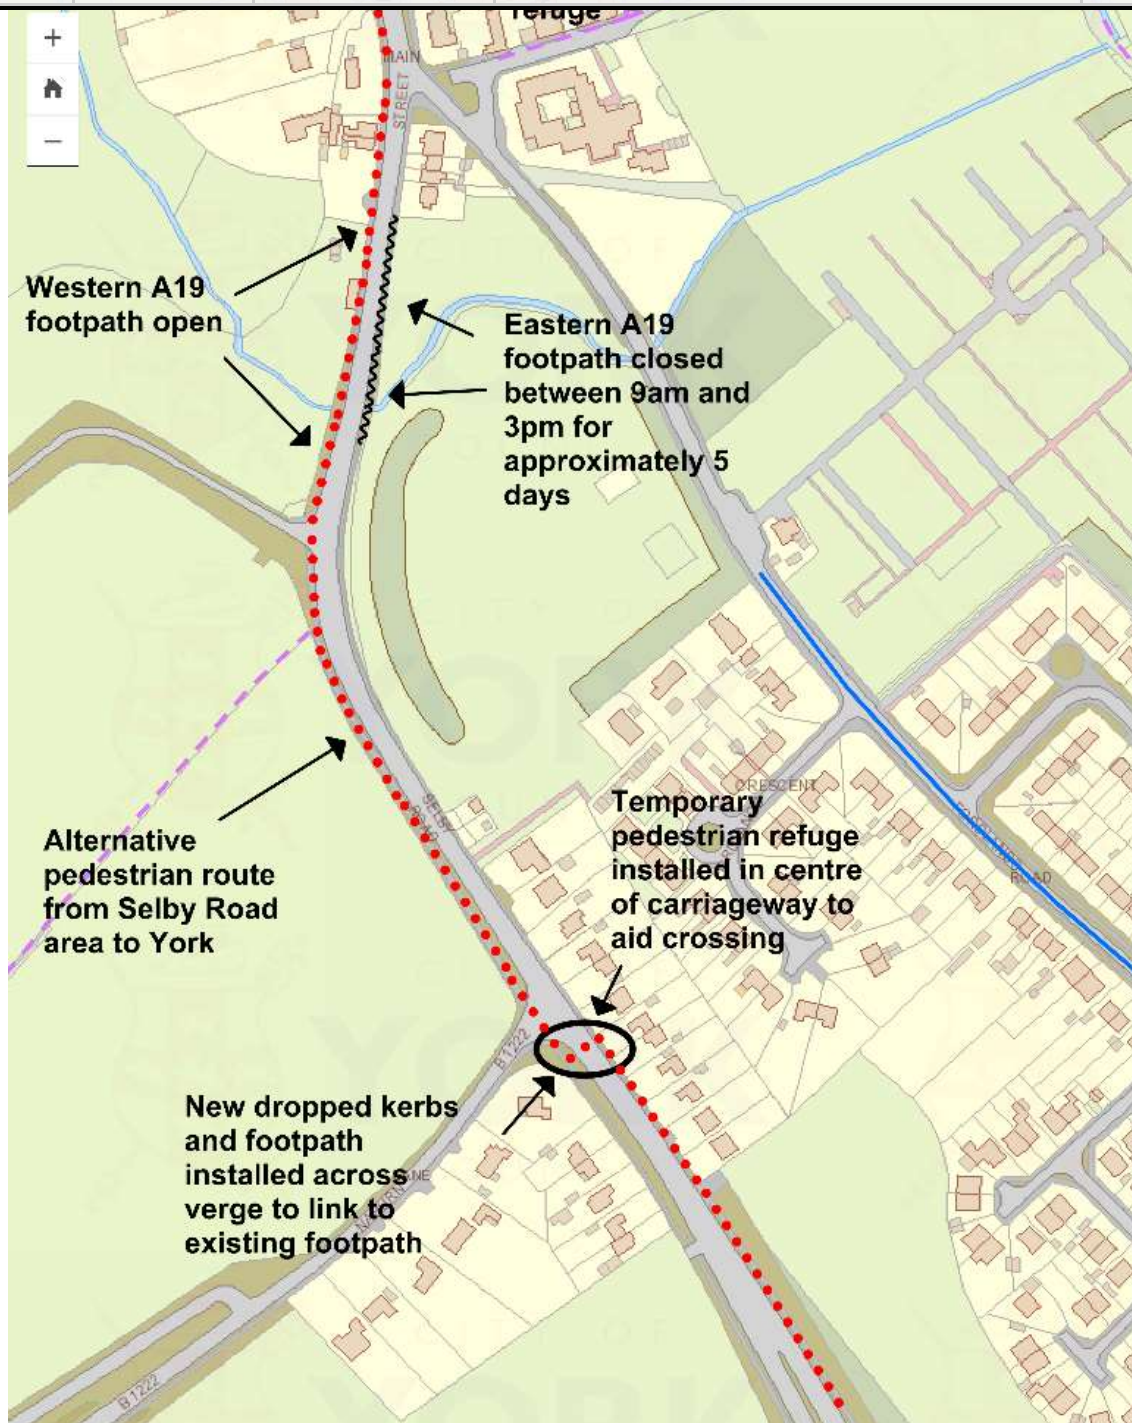

Safety for children and the wider public.

Please be assured that the different areas of works will be securely fenced at all times to ensure the safety of the public.

We will be receiving few deliveries to site this week. Each delivery will be guided into site by one of our employees once traffic and pedestrians are clear from the site entrance. Please be patient if you are held up for a short time whilst these manoeuvres take place.

Pedestrians will be given right of way along the footpaths of Fordlands Road but please be aware of deliveries using the entrances to site off Fordlands Road on occasion.

Copyright © 2017 Howard Civil Engineering, All rights reserved.

Want to change how you receive these emails?
You can [update your preferences](#) or [unsubscribe from this list](#)

